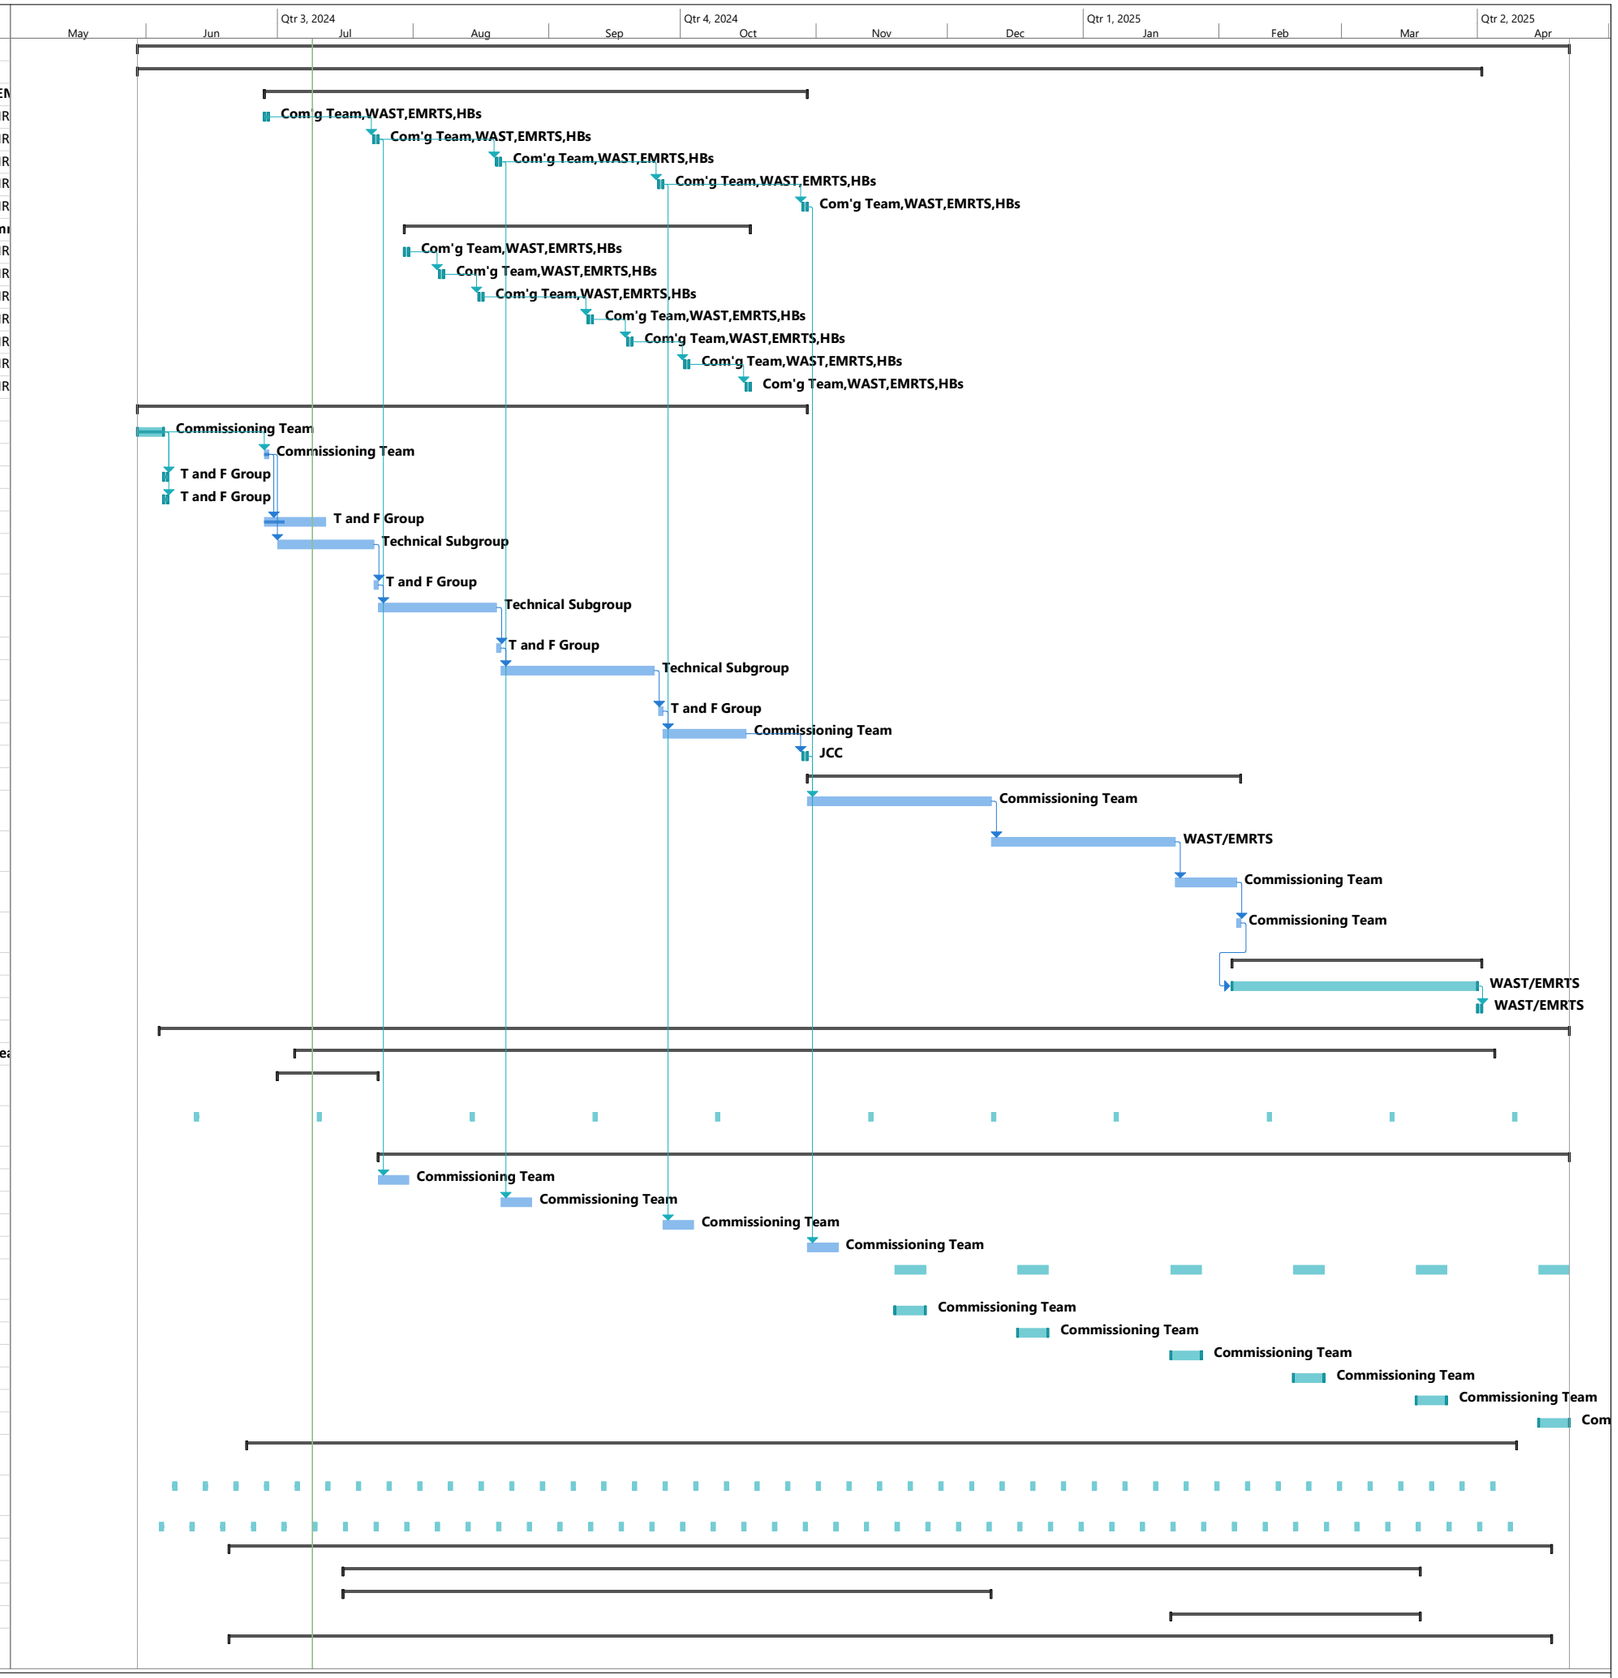ID	Task Mode	Task Name	Duration	Start	Finish	Predec	% Complete	Resource Names
1		**EMRTS Service Review**	**233 da**	**Thu 30/05/24**	**Mon 21/04/25**		**6%**	**JCC**
2		**Recommendation 4 - Bespoke serv**	**219 da**	**Thu 30/05/24**	**Tue 01/04/25**		**5%**	**JCC**
3		**R4 Task and Finish Group Meeti**	**88 day**	**Fri 28/06/24**	**Tue 29/10/24**		**20%**	**Comm'g Team,WAST,EM**
4		June	1 day	Fri 28/06/24	Fri 28/06/24		100%	Com'g Team,WAST,EMR
5		July	1 day	Tue 23/07/24	Tue 23/07/24	4	0%	Com'g Team,WAST,EMR
6		August	1 day	Tue 20/08/24	Tue 20/08/24	5	0%	Com'g Team,WAST,EMR
7		September	1 day	Thu 26/09/24	Thu 26/09/24	6	0%	Com'g Team,WAST,EMR
8		October	1 day	Tue 29/10/24	Tue 29/10/24	7	0%	Com'g Team,WAST,EMR
9		**R4 Technical Sub Group meeting**	**57 day**	**Tue 30/07/24**	**Wed 16/10/24**		**0%**	**WAST,EMRTS,HBs,Com**
10		July	1 day	Tue 30/07/24	Tue 30/07/24		0%	Com'g Team,WAST,EMR
11		August 1	1 day	Wed 07/08/24	Wed 07/08/24	10	0%	Com'g Team,WAST,EMR
12		August 2	1 day	Fri 16/08/24	Fri 16/08/24	11	0%	Com'g Team,WAST,EMR
13		September 1	1 day	Tue 10/09/24	Tue 10/09/24	12	0%	Com'g Team,WAST,EMR
14		September 2	1 day	Thu 19/09/24	Thu 19/09/24	13	0%	Com'g Team,WAST,EMR
15		October 1	1 day	Wed 02/10/24	Wed 02/10/24	14	0%	Com'g Team,WAST,EMR
16		October 2	1 day	Wed 16/10/24	Wed 16/10/24	15	0%	Com'g Team,WAST,EMR
17		**R4 Development**	**109 da**	**Thu 30/05/24**	**Tue 29/10/24**		**10%**	**T and F Group**
18		Receive HB nominations	4 days	Thu 30/05/24	Tue 04/06/24		100%	Commissioning Team
19		Establish T and F Group	1 day	Fri 28/06/24	Fri 28/06/24	18	100%	Commissioning Team
20		Agree membership	1 day	Wed 05/06/24	Wed 05/06/24	18	100%	T and F Group
21		Agree TOR	1 day	Wed 05/06/24	Wed 05/06/24	18	100%	T and F Group
22		Establish Technical Sub Group	10 day	Fri 28/06/24	Thu 11/07/24	19	25%	T and F Group
23		Develop clinical response criteria	16 days	Mon 01/07/24	Mon 22/07/24	19	0%	Technical Subgroup
24		Agree clinical response criteria	1 day	Tue 23/07/24	Tue 23/07/24	23	0%	T and F Group
25		Modelling to define base locations	19 days	Wed 24/07/24	Mon 19/08/24	24	0%	Technical Subgroup
26		Agree base locations	1 day	Tue 20/08/24	Tue 20/08/24	25	0%	T and F Group
27		Operational model development	25 days	Wed 21/08/24	Tue 24/09/24	26	0%	Technical Subgroup
28		Agree operational model	1 day	Thu 26/09/24	Thu 26/09/24	27	0%	T and F Group
29		Recommendations to JCC	13 day	Fri 27/09/24	Tue 15/10/24	28	0%	Commissioning Team
30		Recommendations approved	1 day	Tue 29/10/24	Tue 29/10/24	29	0%	JCC
31		**R4 Commissioning**	**71 day**	**Wed 30/10/24**	**Wed 05/02/25**		**0%**	**JCC**
32		Develop and issue Commissioning Intentions	30 days	Wed 30/10/24	Tue 10/12/24	30	0%	Commissioning Team
33		Comments/response from service	30 days	Wed 11/12/24	Tue 21/01/25	32	0%	WAST/EMRTS
34		Finalise Commissioning Intentions	10 days	Wed 22/01/25	Tue 04/02/25	33	0%	Commissioning Team
35		Formal issue of Commissioning Intentions	1 day	Wed 05/02/25	Wed 05/02/25	34	0%	Commissioning Team
36		**R4 Implementation**	**41 day**	**Tue 04/02/25**	**Tue 01/04/25**		**0%**	**WAST/EMRTS**
37		Service Implementation	40 day	Tue 04/02/25	Mon 31/03/25	35	0%	WAST/EMRTS
38		Go live 1 April 2025	1 day	Tue 01/04/25	Tue 01/04/25	37	0%	WAST/EMRTS
39		**Communication and Engagement**	**230 da**	**Tue 04/06/24**	**Mon 21/04/25**		**7%**	
40		**Monthly Newsletters R4**	**196 da**	**Fri 05/07/24**	**Fri 04/04/25**		**10%**	**Comms Engagement Lea**
51		**Joint Communication and Engagement Plan**	**17 days**	**Mon 01/07/24**	**Tue 23/07/24**		**6%**	**Comms Engagement Leads**
58		**Comms and Engagement Leads Checkpoint**	**216 days**	**Wed 12/06/24**	**Wed 09/04/25**		**9%**	**JCC and HB Comms Leads**
70		**Engagement with Llais**	**194 da**	**Wed 24/07/24**	**Mon 21/04/25**		**0%**	**Commissioning Team**
71		Post July T and F Group	5 days	Wed 24/07/24	Tue 30/07/24	5	0%	Commissioning Team
72		Post August T and F Group	5 days	Wed 21/08/24	Tue 27/08/24	6	0%	Commissioning Team
73		Post September T and F Group	5 days	Fri 27/09/24	Thu 03/10/24	7	0%	Commissioning Team
74		Post October T and F Group	5 days	Wed 30/10/24	Tue 05/11/24	8	0%	Commissioning Team
75		**Ongoing Engagement with Llais**	**110 days**	**Tue 19/11/24**	**Mon 21/04/25**		**0%**	**Commissioning Team**
76		Ongoing Engagement with L	5 days	Tue 19/11/24	Mon 25/11/24		0%	Commissioning Team
77		Ongoing Engagement with L	5 days	Tue 17/12/24	Mon 23/12/24		0%	Commissioning Team
78		Ongoing Engagement with L	5 days	Tue 21/01/25	Mon 27/01/25		0%	Commissioning Team
79		Ongoing Engagement with L	5 days	Tue 18/02/25	Mon 24/02/25		0%	Commissioning Team
80		Ongoing Engagement with L	5 days	Tue 18/03/25	Mon 24/03/25		0%	Commissioning Team
81		Ongoing Engagement with L	5 days	Tue 15/04/25	Mon 21/04/25		0%	Commissioning Team
82		**Regular Catch Up Meetings with WAST and EMRTS**	**208 days**	**Mon 24/06/24**	**Wed 09/04/25**		**6%**	**Commissioning Team,WAST and**
101		**Weekly Meetings with Charity and EMRTS**	**216 days**	**Fri 07/06/24**	**Fri 04/04/25**		**11%**	**Commissioning Team,Charity and**
146		**Comissioning Team Weekly Mee**	**221 da**	**Tue 04/06/24**	**Tue 08/04/25**		**11%**	**Commissioning Team**
192		**Governance and Reporting**	**216 da**	**Thu 20/06/24**	**Thu 17/04/25**		**14%**	**JCC**
193		**JCC Meetings**	**176 da**	**Tue 16/07/24**	**Tue 18/03/25**		**13%**	**JCC**
194		**2024**	**106 da**	**Tue 16/07/24**	**Tue 10/12/24**		**17%**	**JCC**
201		**2025**	**41 day**	**Tue 21/01/25**	**Tue 18/03/25**		**0%**	**JCC**
204		**Interim Ambulance and 111 Commissioning Group**	**216 days**	**Thu 20/06/24**	**Thu 17/04/25**		**17%**	**JCC**
