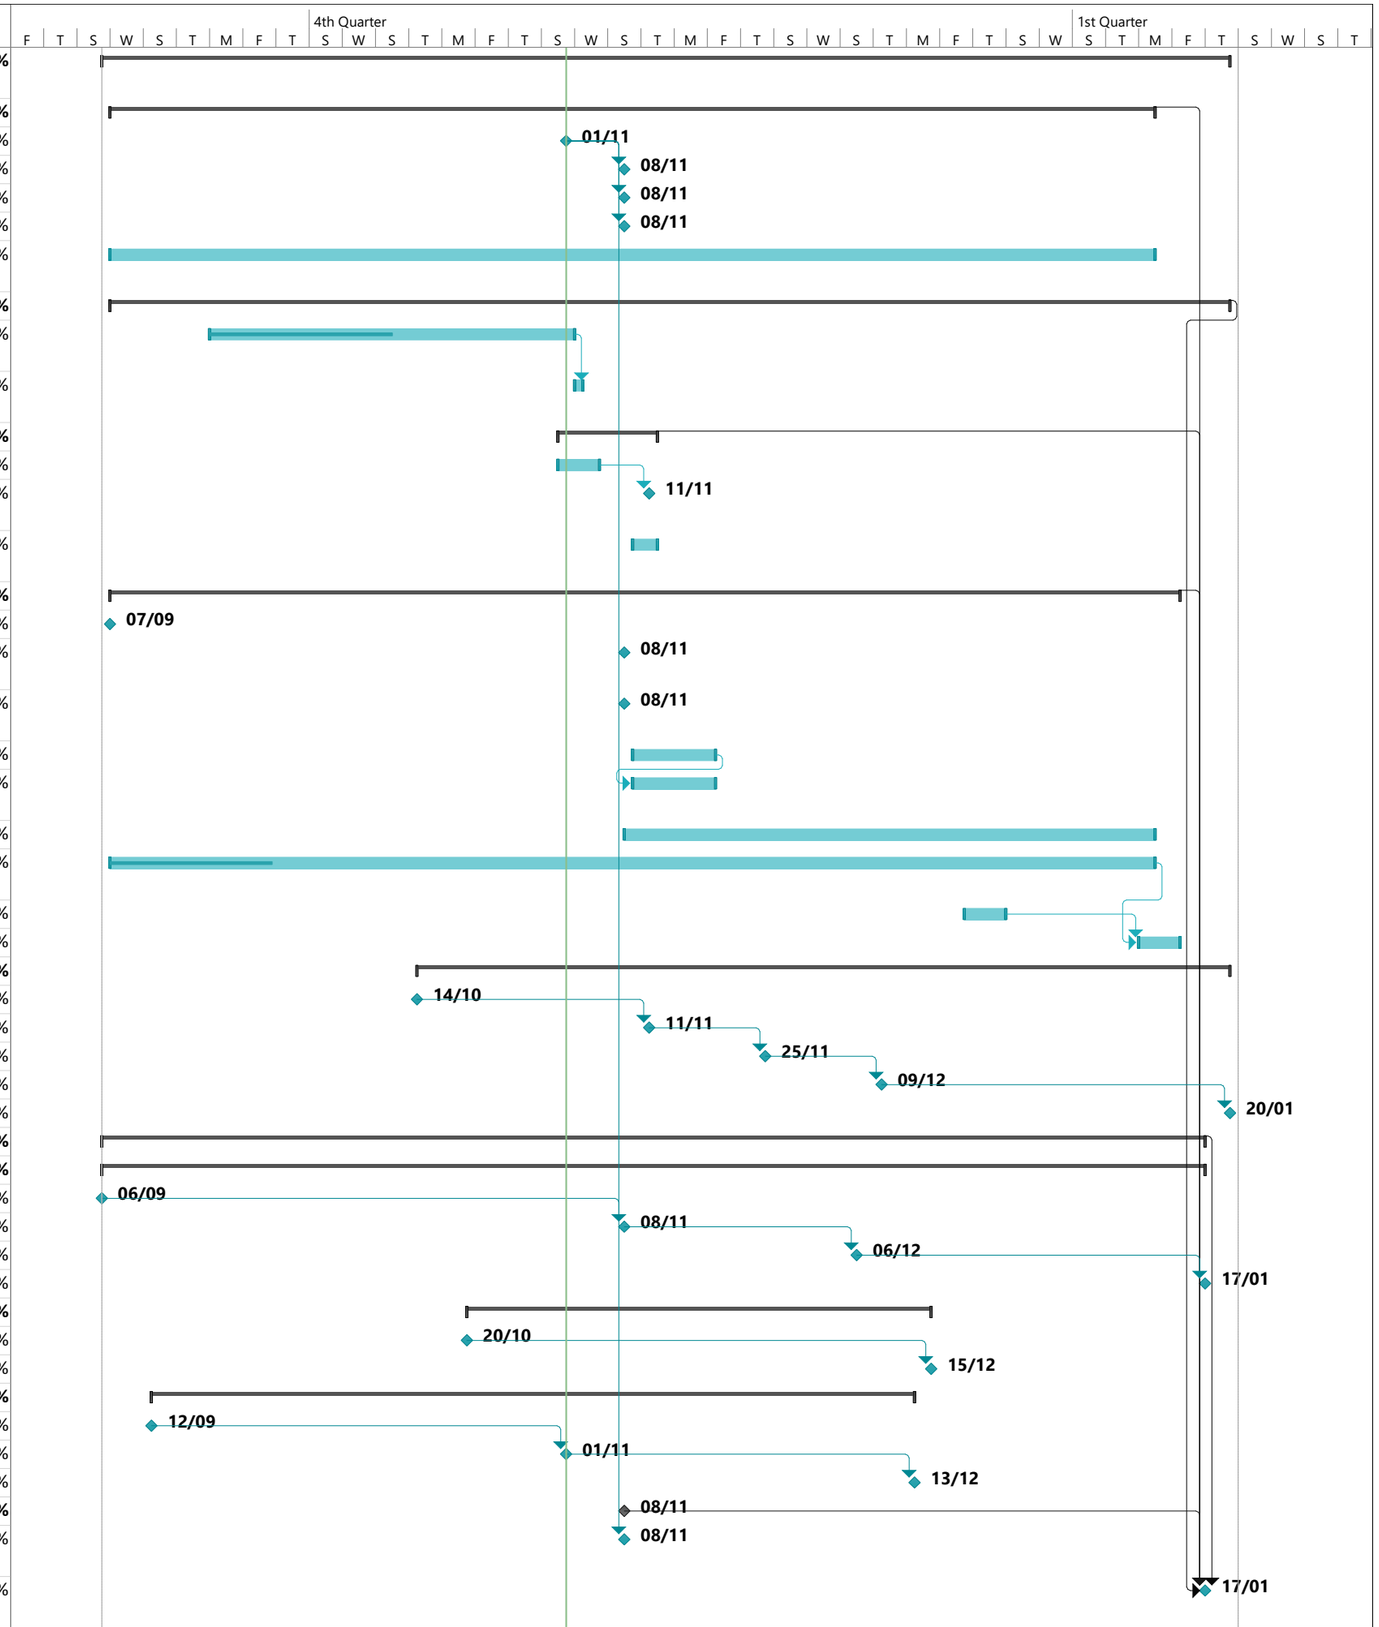ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete
1		**EMRTS/WAA Service Development Proposal**	**98 days?**	**Tue 06/09/22**	**Fri 20/01/23**		**10%**
2		**Service Development Proposal (SDP)**	**90 days**	**Wed 07/09/2**	**Tue 10/01/23**		**0%**
3		Circulation of SDP with EASC papers	0 days	Tue 01/11/22	Tue 01/11/22		100%
4		Presentation to EASC 8 November	0 days	Tue 08/11/22	Tue 08/11/22	3	0%
5		Make available to public	0 days	Tue 08/11/22	Tue 08/11/22	3	0%
6		Request for further info from EASC	0 days	Tue 08/11/22	Tue 08/11/22	3	0%
7		Request from stakeholders through process	90 days	Wed 07/09/22	Tue 10/01/23		0%
8		**Comms and Engagement**	**97 days?**	**Wed 07/09/2**	**Fri 20/01/23**		**15%**
9		Draft communication and engagement plan	32 days	Mon 19/09/22	Tue 01/11/22		50%
10		Finalise communication and engagement plan	1 day?	Wed 02/11/22	Wed 02/11/22	9	0%
11		**Preparation of engagement materials**	**10 days**	**Mon 31/10/2**	**Fri 11/11/22**		**0%**
12		Draft materials for comment	5 days	Mon 31/10/2	Fri 04/11/22		0%
13		Agreement of NHS Wales engagement materials	0 days	Fri 11/11/22	Fri 11/11/22	12	0%
14		Agreement of CHC engagement materials	3 days	Wed 09/11/22	Fri 11/11/22		0%
15		**Working with HBs and CHCs**	**93 days**	**Wed 07/09/2**	**Fri 13/01/23**		**8%**
16		Commence communication	0 days	Wed 07/09/2	Wed 07/09/2		0%
17		Approval to commence formal public engagement	0 days	Tue 08/11/22	Tue 08/11/22		0%
18		Approval to commence EASC scrutiny	0 days	Tue 08/11/22	Tue 08/11/22		0%
19		Confirm programme of engagement	8 days	Wed 09/11/2	Fri 18/11/22		0%
20		Agree dates, provide appropriate notice	8 days	Wed 09/11/22	Fri 18/11/22	19	0%
21		Formal public engagement	46 days	Tue 08/11/22	Tue 10/01/23		0%
22		Collation and analysis of feedback received	90 days	Wed 07/09/22	Tue 10/01/23		15%
23		Mid process review	5 days	Mon 19/12/2	Fri 23/12/22		0%
24		End of process update	5 days	Mon 09/01/2	Fri 13/01/23	22,23	0%
25		**Briefing Notes**	**70 days**	**Fri 14/10/22**	**Fri 20/01/23**		**0%**
26		Briefing Note 1	0 days	Fri 14/10/22	Fri 14/10/22		100%
27		Briefing Note 2	0 days	Fri 11/11/22	Fri 11/11/22	26	0%
28		Briefing Note 3	0 days	Fri 25/11/22	Fri 25/11/22	27	0%
29		Briefing Note 4	0 days	Fri 09/12/22	Fri 09/12/22	28	0%
30		Briefing Note 5	0 days	Fri 20/01/23	Fri 20/01/23	29	0%
31		**Governance and Reporting**	**95 days**	**Tue 06/09/2**	**Tue 17/01/23**		**0%**
32		**EASC Committee**	**95 days**	**Tue 06/09/2**	**Tue 17/01/23**		**0%**
33		EASC Committee 6 Sept	0 days	Tue 06/09/22	Tue 06/09/22		100%
34		EASC Committee 8 Nov	0 days	Tue 08/11/22	Tue 08/11/22	33	0%
35		EASC Committee 6 Dec	0 days	Tue 06/12/22	Tue 06/12/22	34	0%
36		EASC Committee 17 Jan	0 days	Tue 17/01/23	Tue 17/01/23	35	0%
37		**EASC Management Group**	**40 days**	**Thu 20/10/2**	**Thu 15/12/2**		**0%**
38		EASC Mgt Group 20 Oct	0 days	Thu 20/10/22	Thu 20/10/22		100%
39		EASC Mgt Group 15 Dec	0 days	Thu 15/12/22	Thu 15/12/22	38	0%
40		**EMRTS DAG**	**66 days**	**Mon 12/09/2**	**Tue 13/12/2**		**0%**
41		EMRTS DAG 12 Sept	0 days	Mon 12/09/2	Mon 12/09/2		100%
42		EMRTS DAG 1 Nov	0 days	Tue 01/11/22	Tue 01/11/22	41	0%
43		EMRTS DAG 13 Dec	0 days	Tue 13/12/22	Tue 13/12/22	42	0%
44		**Risk Management**	**0 days**	**Tue 08/11/2**	**Tue 08/11/2**		**0%**
45		Consideration and discussion of commissioning risks	0 days	Tue 08/11/22	Tue 08/11/22	3	0%
46		Commissioning decision by EASC members	0 days	Tue 17/01/23	Tue 17/01/23	2,8,11,15,31,	0%
